

SKETCH OF PROPOSED WORK


(SHOW STREET NAMES AND HOUSE NO.'S WITH APPROXIMATE WORK LOCATIONS)

APPROVED BY: _____
 ASPINWALL BOROUGH SECRETARY

DATE PERMIT ISSUED: _____

CHECK LIST

CERTIFICATE OF INSURANCE	_____	
PERFORMANCE BOND	_____	
LIST OF RESIDENTS AFFECTED	_____	
DEPOSIT PAID	_____	
NOTIFICATION OF COMPLETION	_____	DATE _____
INTERIM INSPECTION REPORT ISSUED	_____	DATE _____
FINAL INSPECTION REPORT ISSUED	_____	DATE _____

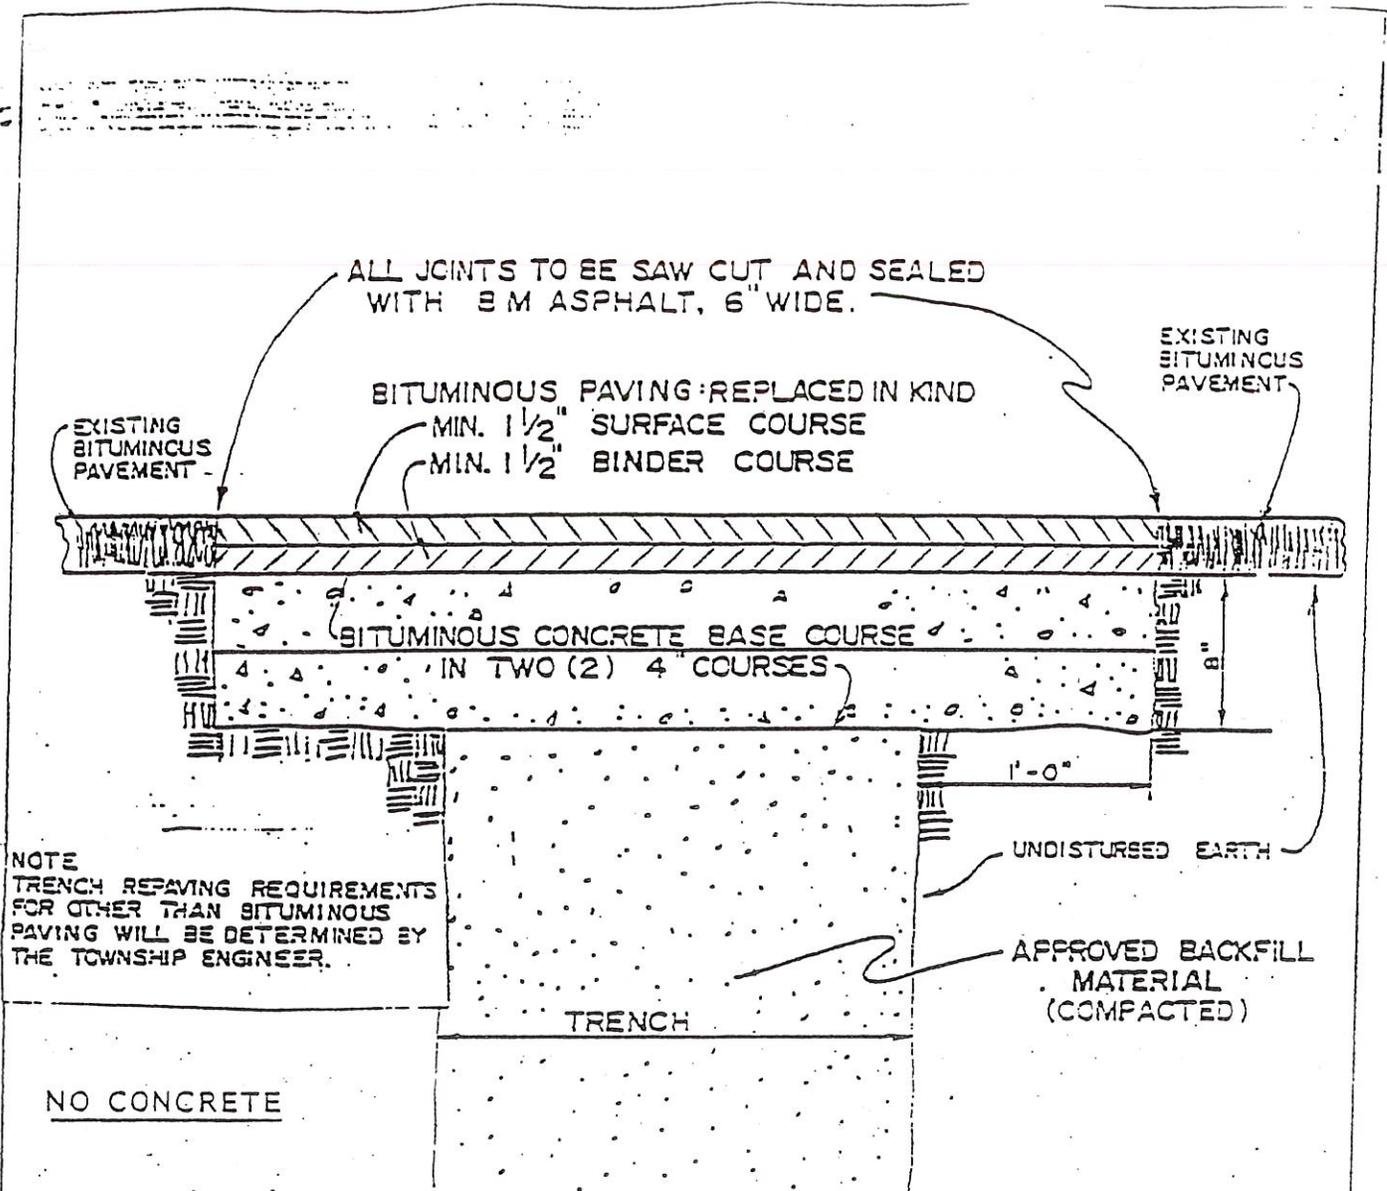

NOTE
 TRENCH REPAVING REQUIREMENTS
 FOR OTHER THAN BITUMINOUS
 PAVING WILL BE DETERMINED BY
 THE TOWNSHIP ENGINEER.

NO CONCRETE

ALL MATERIAL USED SHALL CONFORM TO PENNSYLVANIA DEPARTMENT OF TRANSPORTATION
 PUB. 408 SPECIFICATIONS.

ALL DRIVEWAYS, WALKWAYS, SIDEWALKS, STEPS, LAWNS, ETC. DISTURBED SHALL BE
 REPLACED IN KIND WITH THE FOLLOWING MINIMUMS:

BITUMINOUS DRIVEWAYS-COMpletely TAMPED STONE OR GRAVEL BACKFILL, 4" BITUMINOUS
 CONCRETE BASE COURSE WITH 1 1/2" WEARING COURSE.

CONCRETE DRIVEWAYS-COMpletely TAMPED STONE OR GRAVEL BACKFILL, 6" REINFORCED
 CONCRETE.

SIDEWALKS-5" PLAIN CONCRETE.


BERM AREAS DISTURBED SHALL BE REPLACED WITH TAMPED STONE OR GRAVEL BACKFILL
 UP TO A 45° ANGLE FROM THE ROAD METAL AND THEN WITH TAMPED EARTH. THE TOP
 6" OF MATERIAL SHALL BE REPLACED IN KIND.


REVISION:

TRENCH REPAVING
 FOR
 BITUMINOUS PAVING

THE BOROUGH OF ASPINWALL

CONCRETE SURFACE RECONST.

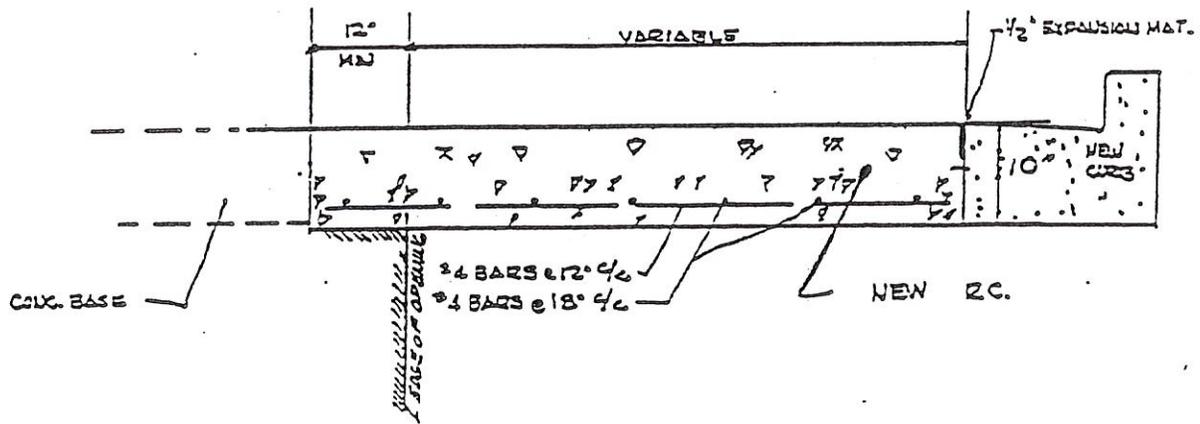

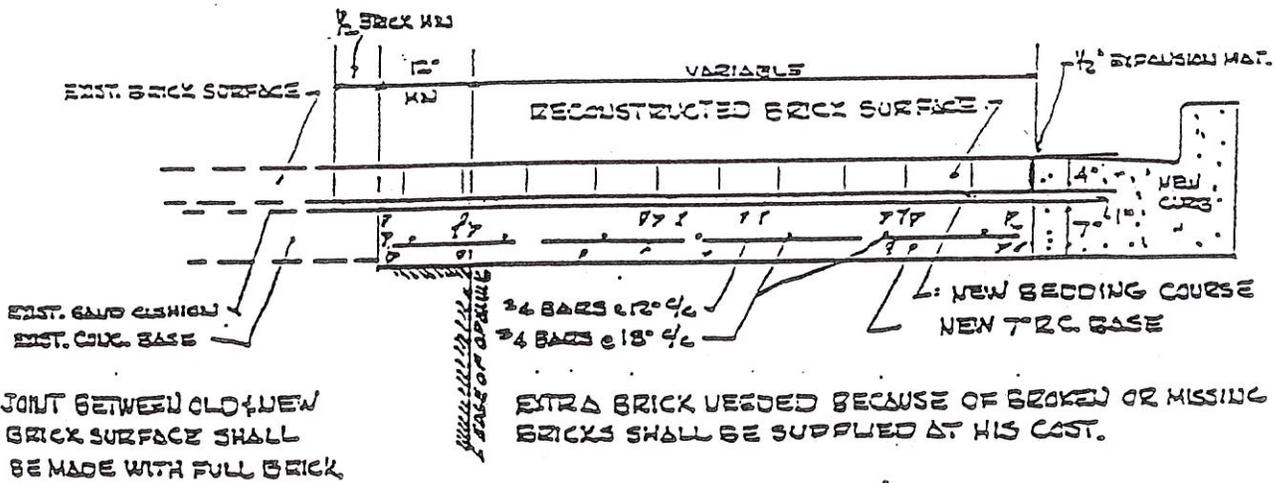

BRICK SURFACE RECONST. & CONCRETE BASE DETAIL

NO CONCRETE BASE
